

Community Update: September 2019

Who to contact



Site Manager

Henry Brooks
07957 176518

blossomstreet@cantillon.co.uk

Project Manager

Malcolm Bredenkamp
blossomstreet@cantillon.co.uk

Out of Hours Security

Omni Security
0800 9178971

Cantillon Head Office
01923 255 256

Considerate Constructors Scheme
0800 783 1423



What we've been doing

Dear Neighbours

Welcome to our sixth monthly newsletter from the on-site delivery team. We are pleased to report that works continue to progress well.

Work is well underway to the structures on 14-17 Blossom Street and 13-14 Norton Folgate where we are retaining the existing facades.

We have started to install rotary bored concrete mini pile foundations to the rear of the Network Rail Retaining wall.

Archaeological excavations by MOLA in 10 Shoreditch High Street.

What we will be doing in the next month

Installation of bored piles and Archaeology

We will continue to install rotary bored concrete mini pile foundations to the rear of the Network Rail Retaining Wall.

Existing archaeological excavations continue with additional areas of site being made available for this work as they are freed up by the preceding demolition.

Sheet piling

We will install sheet piles along the northern boundary of Fleur de Lis Passage as enabling works for the archaeological excavation. The sheets will be installed utilising a piling rig which minimises vibration or noise from this operation.

Demolition works

Demolition to the low-level structures are to commence along the Network Rail boundary.

We will complete the façade retention works to 14-15 Blossom Street and 15-16 Norton Folgate.

In addition, the demolition to the concrete structures of 13 Norton Folgate and 17 Blossom Street will be concluded.




Construction Update meetings

Thank you to everyone who attended last month's community update meeting. We discussed a number of matters, including:

- Site works and progress.
- Out of hours delivery of heavy machinery.
- Suspension of the bus stop on Blossom Street, which will be subject to a separate newsletter once the date is determined.
- Planned activities over the next month.

Next meeting: Thursday 26 September, 6.15 pm at Loom Court, E1 6PL

We will be updating you on the progress of works and will be available to assist with any questions you may have.

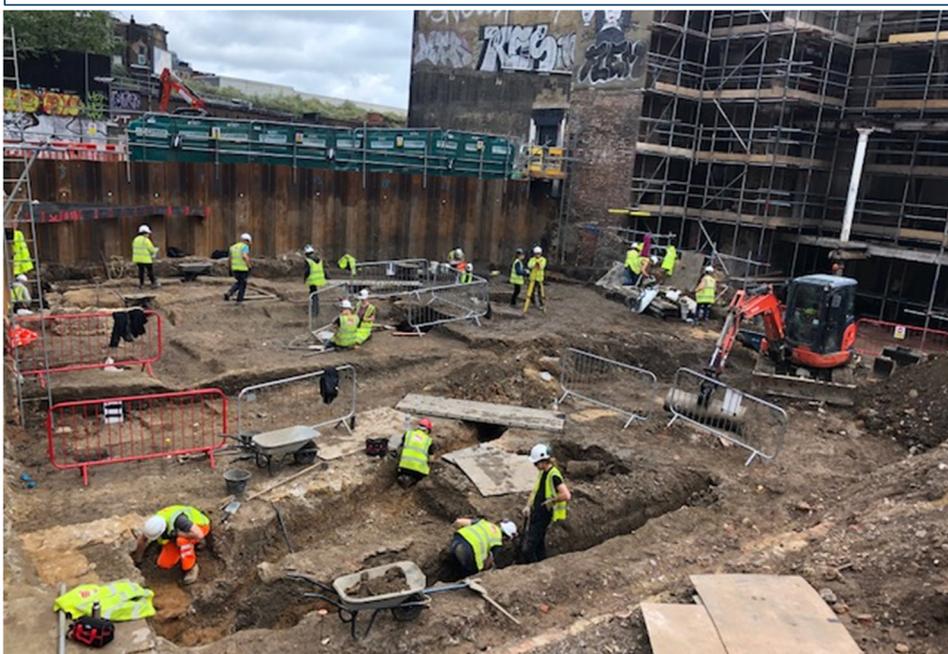

Key upcoming activities and outline timescales

- Continuing demolition to the Blossom Street and Norton Folgate elevations.
- Rotary bored pile installation adjacent the Network Rail Retaining wall.
- Archaeological excavation continues in September to the former buildings along Shoreditch High Street.
- Demolition adjacent the Network Rail Boundary continues.
- Excavator to be collected from Site on the evening of Monday 9th September, between 7:30pm and 8pm, from the site gates located at Shoreditch High Street.
